



## ACCOMPLISHMENT REPORT

<b>I. PROJECT ACTIVITY:</b>	<b>IMPROVEMENT OF MAINLINE PIPE THROUGH PARALLEL PIPING AT BRGY. VILLAROSA</b>
<b>II. LEAD IMPLEMENTATION AGENCY:</b>	LICAB WATER DISTRICT
<b>III. PROJECT OBJECTIVE:</b>	TO IMPROVE THE LINE PRESSURE IN PUROK 1, 2 AND 3 OF BARANGAY VILLAROSA.
<b>IV. ESIMATED COST:</b>	ESTIMATED TOTAL COST OF PROJECT: <b>449,280.00</b>
<b>V. ACTUAL COST:</b>	ACTUAL TOTAL COST OF PROJECT: <b>593,521.13</b>
<b>VI. PROJECT LOCATION:</b>	BARANGAY VILLAROSA
<b>VII. TARGET BENEFICIARY:</b>	THE PROJECT AIMS TO CONTINUOUSLY PROVIDE SAFE AND POTABLE WATER BY MAINTAINING THE PIPELINE SYSTEM.
<b>VIII. BRIEF PROJECT DESCRIPTION:</b>	LAYING OF PARALLEL PIPES
<b>IX. TARGET IMPLEMENTATION:</b>	THE PROJECT WAS ACCOMPLISHED AFTER 73 DAYS. Date Started: September 18, 2024 Date Completed: <b>November 30, 2024</b>

Prepared by:

  
**RIA FE M. NARNE**  
SENIOR ENGINEER A

Approved by:

  
**ANNE LORELIE DL. LAURETA**  
General Manager – Licab Water District



**Accomplishment Report**  
As of November 30, 2024

**Summary**

The Licab Water District Engineering Unit have inspected and checked the **completion of IMPROVEMENT OF MAINLINE PIPE THROUGH PARALLEL PIPING AT BRGY. VILLAROSA** at Barangay Villarosa, Licab, Nueva Ecija by the first party and hereby attest the **100.00 %** completed.


**Basis of Work Completion** (set by Engineering unit)

60%	Trenching
40%	Embankment
Total of 100% when work is completed	


**Current Progress of Construction**

60%	Trenching
40%	Embankment
Total of 100.00% of work is completed.	

Prepared by:

  
**RIA FE M. NARNE**  
SENIOR ENGINEER A

Approved by:

  
**ANNE LORELIE DL. LAURETA**  
General Manager – Licab Water District





LICAB WATER DISTRICT  
Real St., Poblacion, Sur, Licab Nueva Ecija  
[licabwd@yahoo.com](mailto:licabwd@yahoo.com)  
(09258158581-3)



QMS 19 93 0026

**Accomplishment Report**  
As of October 08, 2024

**Summary**

The Licab Water District Engineering Unit have inspected and checked the **completion of IMPROVEMENT OF MAINLINE PIPE THROUGH PARALLEL PIPING AT BRGY. VILLAROSA** at Barangay Villarosa, Licab, Nueva Ecija by the first party and hereby attest the **97.00 %** completed.


**Basis of Work Completion** (set by Engineering unit)

60%	Trenching
40%	Embankment
Total of 100% when work is completed	


**Current Progress of Construction**

59%	Trenching
38%	Embankment
Total of 97.00% of work is completed.	

Prepared by:

  
**RIA FE M. NARNE**  
SENIOR ENGINEER A

Approved by:

  
**ANNE LORELIE DL. LAURETA**  
General Manager – Licab Water District





LICAB WATER DISTRICT  
Real St., Poblacion, Sur, Licab Nueva Ecija  
[licabwd@yahoo.com](mailto:licabwd@yahoo.com)  
(09258158581-3)



QMS 19 93 0026

**Accomplishment Report**  
As of September 27, 2024

**Summary**

The Licab Water District Engineering Unit have inspected and checked the **completion of IMPROVEMENT OF MAINLINE PIPE THROUGH PARALLEL PIPING AT BRGY. VILLAROSA** at Barangay Villarosa, Licab, Nueva Ecija by the first party and hereby attest the **32.20 %** completed.


**Basis of Work Completion** (set by Engineering unit)

60%	Trenching
40%	Embankment
Total of 100% when work is completed	

**Current Progress of Construction**

19.32%	Trenching
12.88%	Embankment
Total of 32.20% of work is completed.	

Prepared by:

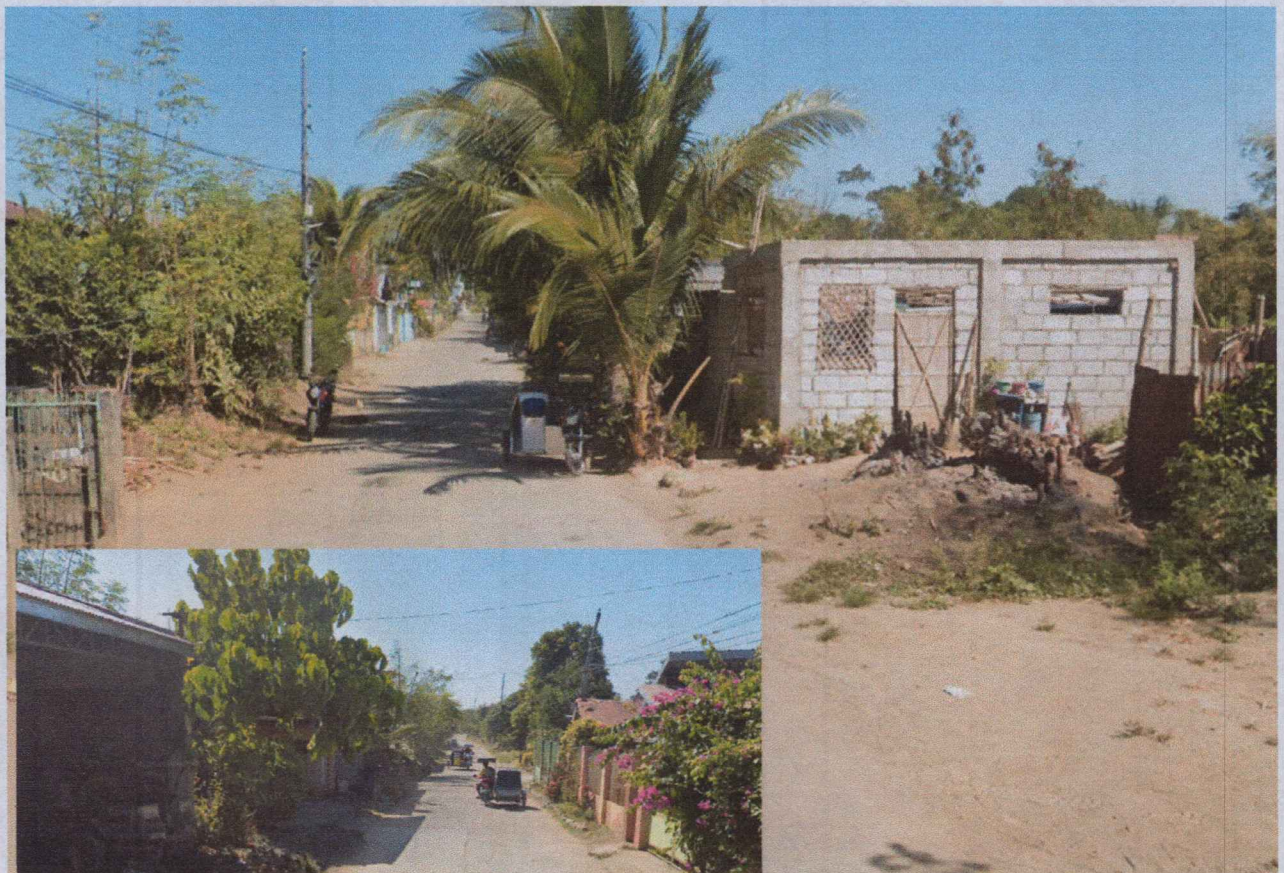
  
**RIA FE M. NARNE**  
SENIOR ENGINEER A

Approved by:

  
**ANNE LORELIE DL. LAURETA**  
General Manager – Licab Water District



## ACCOMPLISHMENT REPORT BEFORE

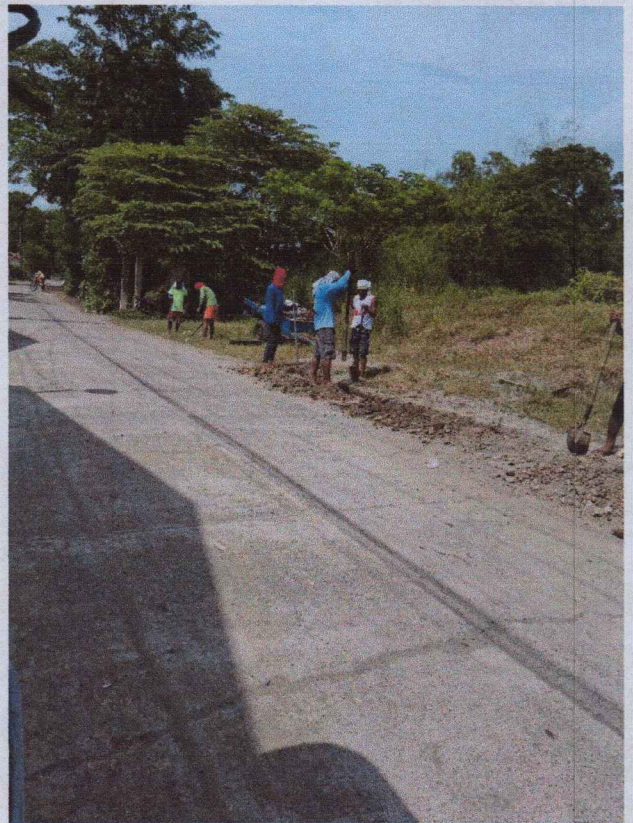




## DURING CONSTRUCTION









## DURING CONSTRUCTION









## AFTER CONSTRUCTION







AVE. PRESSURE (P1 BRGY. VILLAROSA)		
	Before Re-Piping	After Re-Piping
AM (DURING PEAK HOUR) – 8:00am – 12:00pm	3-5 PSI	8-15 PSI
PM (DURING PEAK HOUR) – 6:00pm – 8:00pm	3-5 PSI	10-20 PSI
