



LICAB WATER DISTRICT
Real St., Poblacion, Sur, Licab Nueva Ecija
licabwd@yahoo.com
(09258158581-3)



QMS 19 93 0026

Accomplishment Report
As of June 20, 2024

Summary

The Licab Water District Engineering Unit have inspected and checked the **completion of IMPROVEMENT OF STA. MARIA PUMPING STATION** at Barangay Villarosa, Licab, Nueva Ecija by the first party and hereby attest the **100%** completed.


Basis of Work Completion (set by Engineering unit)

20%	Concrete Works
30%	Steel Works
30%	Roof Frame
20%	Roofing
Total of 100% when work is completed	


Current Progress of Construction

20%	Concrete Works
30%	Steel Works
30%	Roof Frame
20%	Roofing
Total of 100% work is completed	

Prepared by:


RIA FE M. NARNE
SENIOR ENGINEER A


Approved by:


ANNE LORELIE DL. LAURETA
General Manager – Licab Water District


ACCOMPLISHMENT REPORT

I. PROJECT ACTIVITY:	IMPROVEMENT OF STA. MARIA PUMPING STATION
II. LEAD IMPLEMENTATION AGENCY:	LICAB WATER DISTRICT
III. PROJECT OBJECTIVE:	TO MAINTAIN IMPROVE THE ENVIRONMENT OF PUMPING STATION IN ORDER TO CONTINUOUSLY DELIVER GOOD QUALITY SERVICE
IV. ESIMATED COST:	ESTIMATED TOTAL COST OF PROJECT: 34,984.50
V. ACTUAL COST:	ACTUAL TOTAL COST OF PROJECT: 23,187.00
VI. PROJECT LOCATION:	BARANGAY STA. MARIA
VII. TARGET BENEFICIARY:	THE PROJECT AIMS TO CONTINUOUSLY PROVIDE SAFE AND POTABLE WATER BY MAINTAINING THE PIPELINE SYSTEM.
VIII. BRIEF PROJECT DESCRIPTION:	REPAIR OF STA. MARIA PUMPING STATION ATTACHED ROOF AND LAYING OF DRAINPIPES.
IX. TARGET IMPLEMENTATION:	THE PROJECT WAS ACCOMPLISHED AFTER 60 DAYS. Date Started: April 22, 2024 Date Completed: June 20, 2024

Prepared by:


RIA FE M. NARNE
SENIOR ENGINEER A

Approved by:

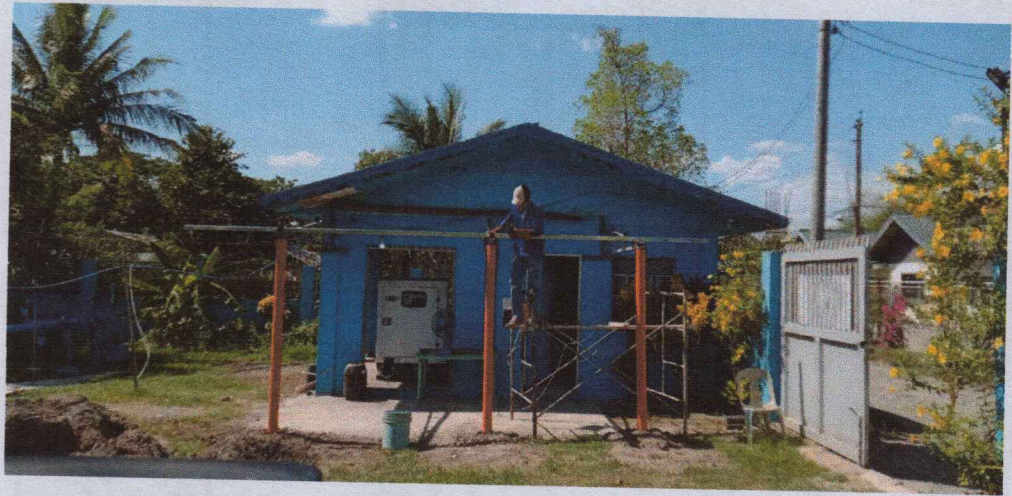
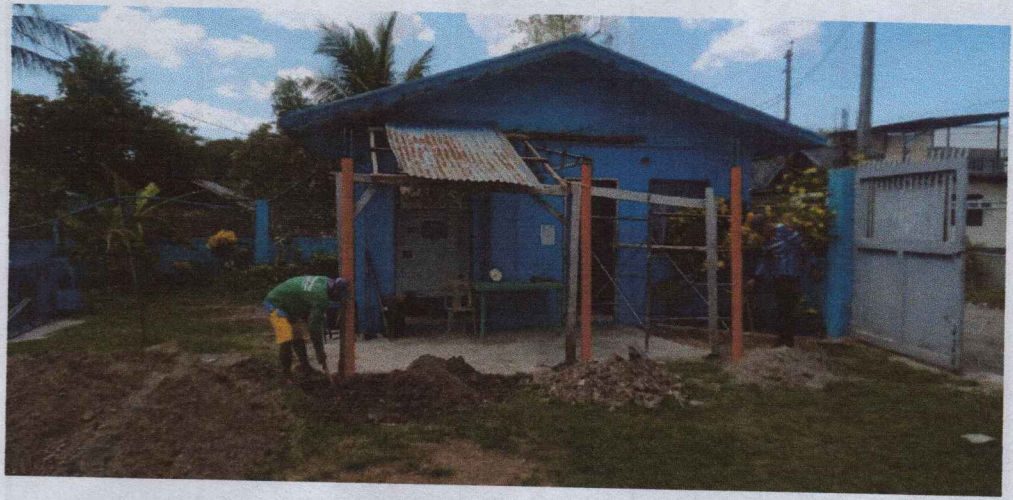

ANNE LORELIE DL. LAURETA
General Manager – Licab Water District

ACCOMPLISHMENT REPORT BEFORE



DURING CONSTRUCTION







AFTER



